Mar-14-26 16:30
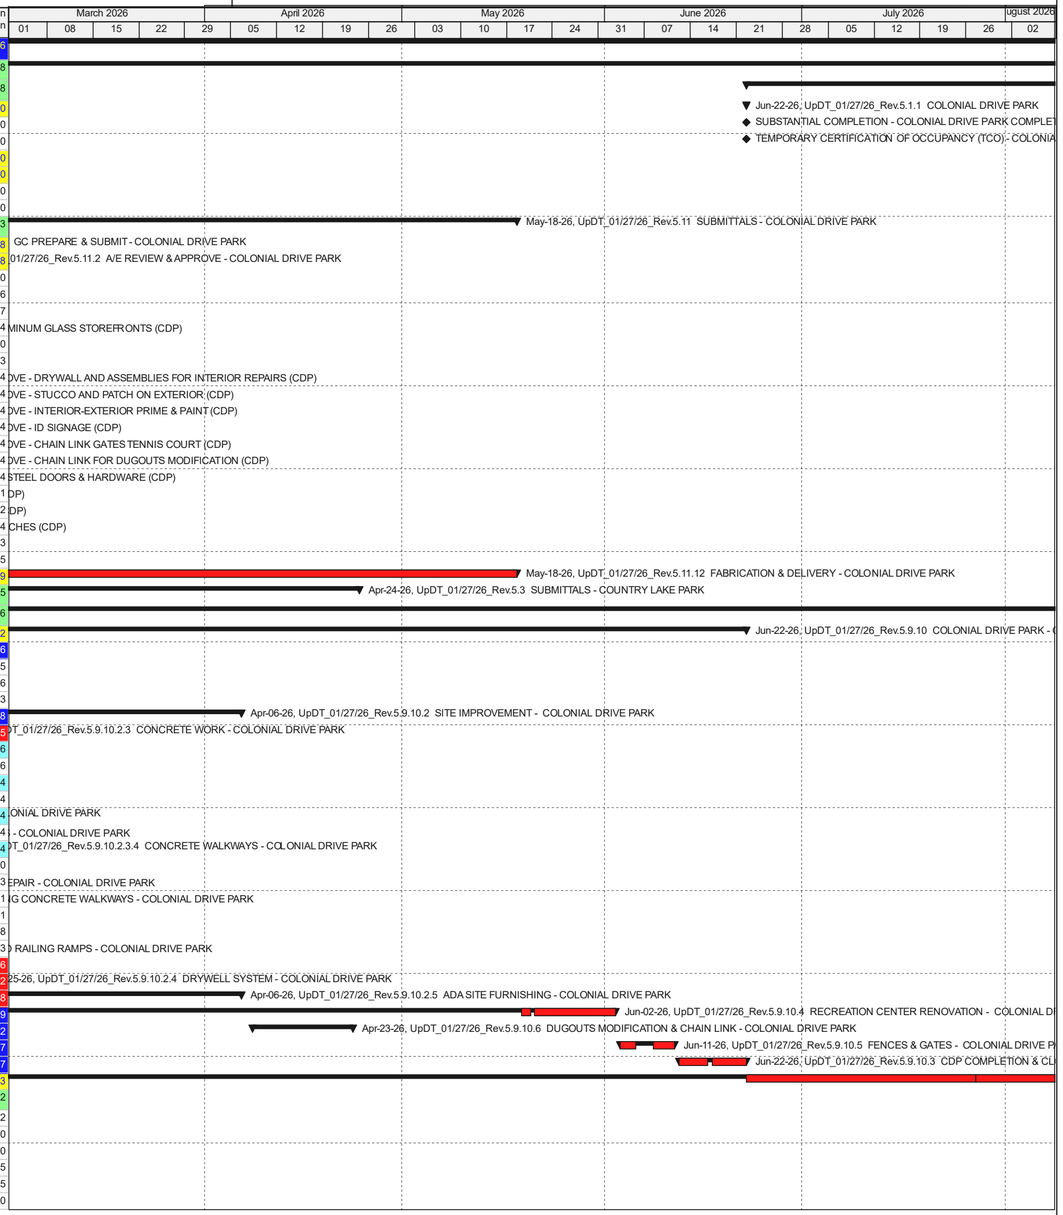
Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Activity Count	Physical % Complete	Activity % Complete	Schedule % Complete	Actual Duration	Actual Start	Actual Finish	Early Start	Early Finish	At Completion Duration
UpDT_01/27/26_Rev.5	COLONIAL DRIVE PARK & CC	398	Sep-08-25 A	Nov-07-26	Oct-06-25	Aug-02-26	0	184			63.94%	142	Sep-08-25		Jan-27-26	Nov-07-26	426
UpDT_01/27/26_Rev.5.7	GENERAL CONDITIONS	301	Oct-06-25 A	Nov-07-26	Oct-06-25	Aug-02-26	0	5			0%	113	Oct-06-25		Jan-27-26	Nov-07-26	398
UpDT_01/27/26_Rev.5.1	PROJECT MILESTONES	138	Jun-22-26	Nov-07-26	Feb-27-26	Aug-02-26	0	6			0%	0			Jun-22-26	Nov-07-26	138
UpDT_01/27/26_Rev.5.1.1	COLONIAL DRIVE PARK	0	Jun-22-26	Jun-22-26	Feb-27-26	Feb-27-26	-19	2			0%	0			Jun-22-26	Jun-22-26	0
MS-CDP-110	SUBSTANTIAL COMPLETION - COLONIAL DRIVE I	0		Jun-22-26		Feb-27-26	-19	1	0%	0%	0%	0				Jun-22-26	0
MS-CDP-100	TEMPORARY CERTIFICATION OF OCCUPANCY (1	0		Jun-22-26		Feb-27-26	-19	1	0%	0%	0%	0				Jun-22-26	0
UpDT_01/27/26_Rev.5.1.2	COUNTRY LAKE PARK	0	Aug-27-26	Aug-27-26	May-22-26	May-22-26	-85	2			0%	0			Aug-27-26	Aug-27-26	0
UpDT_01/27/26_Rev.5.1.3	PROJECT FINAL COMPLETION	60	Sep-08-26	Nov-07-26	Jun-03-26	Aug-02-26	0	2			0%	0			Sep-08-26	Nov-07-26	60
MS-PC-100	PROJECT FINAL SUBSTANTIAL COMPLETION (Jur	0		Sep-08-26		Jun-03-26	0	1	0%	0%	0%	0				Sep-08-26	0
MS-PC-110	PROJECT FINAL COMPLETION	0		Nov-07-26		Aug-02-26	0	1	0%	0%	0%	0				Nov-07-26	0
UpDT_01/27/26_Rev.5.11	SUBMITTALS - COLONIAL	225	Sep-08-25 A	May-18-26	Oct-06-25	Jan-26-26	-76	54			0%	142	Sep-08-25		Jan-27-26	May-18-26	253
UpDT_01/27/26_Rev.5.11.1	GC PREPARE & SUBMIT - COLONIAL	120	Sep-08-25 A	Feb-02-26	Oct-06-25	Nov-17-25	3	18			0%	136	Sep-08-25		Jan-27-26	Feb-02-26	148
UpDT_01/27/26_Rev.5.11.2	A/E REVIEW & APPROVE - COLONIAI	134	Sep-12-25 A	Feb-16-26	Oct-06-25	Dec-01-25	2	18			0%	138	Sep-12-25		Jan-27-26	Feb-16-26	158
SU-CP-142N	REVIEW & APPROVE - CONCRETE MIX (CDP)	3	Oct-27-25 A	Oct-27-25 A	Oct-06-25	Oct-08-25		1	100%	100%	100%	0	Oct-27-25	Oct-27-25	Jan-27-26	Jan-27-26	0
SU-CP-132N	REVIEW & APPROVE - ASPHALT (CDP)	14	Jan-22-26 A	Jan-28-26 A	Oct-06-25	Oct-19-25		1	100%	100%	100%	6	Jan-22-26	Jan-28-26	Jan-27-26	Jan-27-26	6
SU-CP-133N	REVIEW & APPROVE - REBAR (CDP)	3	Sep-12-25 A	Sep-19-25 A	Oct-06-25	Oct-08-25		1	100%	100%	100%	7	Sep-12-25	Sep-19-25	Jan-27-26	Jan-27-26	7
SU-CP-107	REVIEW & APPROVE - ALUMINUM GLASS STORE	14	Jan-27-26	Feb-09-26	Oct-07-25	Oct-20-25	-95	1	0%	0%	100%	0			Jan-27-26	Feb-09-26	14
SU-CP-134N	REVIEW & APPROVE - LIME ROCK (CDP)	14	Oct-27-25 A	Oct-27-25 A	Oct-13-25	Oct-26-25		1	100%	100%	100%	0	Oct-27-25	Oct-27-25	Jan-27-26	Jan-27-26	0
SU-CP-135N	REVIEW & APPROVE - DRAIN WELL (CDP)	14	Oct-31-25 A	Nov-13-25 A	Oct-13-25	Oct-26-25		1	100%	100%	100%	13	Oct-31-25	Nov-13-25	Jan-27-26	Jan-27-26	13
SU-CP-136N	REVIEW & APPROVE - DRYWALL AND ASSEMBLI	14	Feb-03-26	Feb-16-26	Oct-13-25	Oct-26-25	-27	1	0%	0%	100%	0			Feb-03-26	Feb-16-26	14
SU-CP-137N	REVIEW & APPROVE - STUCCO AND PATCH ON E	14	Feb-03-26	Feb-16-26	Oct-13-25	Oct-26-25	-14	1	0%	0%	100%	0			Feb-03-26	Feb-16-26	14
SU-CP-138N	REVIEW & APPROVE - INTERIOR-EXTERIOR PRIN	14	Feb-03-26	Feb-16-26	Oct-13-25	Oct-26-25	-27	1	0%	0%	100%	0			Feb-03-26	Feb-16-26	14
SU-CP-139N	REVIEW & APPROVE - ID SIGNAGE (CDP)	14	Feb-03-26	Feb-16-26	Oct-13-25	Oct-26-25	-27	1	0%	0%	100%	0			Feb-03-26	Feb-16-26	14
SU-CP-140N	REVIEW & APPROVE - CHAIN LINK GATES TENNI	14	Feb-03-26	Feb-16-26	Oct-13-25	Oct-26-25	2	1	0%	0%	100%	0			Feb-03-26	Feb-16-26	14
SU-CP-141N	REVIEW & APPROVE - CHAIN LINK FOR DUGOUT	14	Feb-03-26	Feb-16-26	Oct-13-25	Oct-26-25	-5	1	0%	0%	100%	0			Feb-03-26	Feb-16-26	14
SU-CP-108	REVIEW & APPROVE - HM STEEL DOORS & HARI	14	Jan-27-26	Feb-09-26	Oct-22-25	Nov-04-25	-52	1	0%	0%	100%	0			Jan-27-26	Feb-09-26	14
SU-CP-113	REVIEW & APPROVE - ADA DRINKING FOUNTAIN	14	Jan-22-26 A	Jan-23-26 A	Nov-04-25	Nov-17-25		1	100%	100%	100%	1	Jan-22-26	Jan-23-26	Jan-27-26	Jan-27-26	1
SU-CP-109	REVIEW & APPROVE - ADA HAND RAILING RAMF	14	Jan-21-26 A	Jan-23-26 A	Nov-18-25	Dec-01-25		1	100%	100%	100%	2	Jan-21-26	Jan-23-26	Jan-27-26	Jan-27-26	2
SU-CP-110	REVIEW & APPROVE - BENCHES (CDP)	14	Jan-27-26	Feb-09-26	Nov-18-25	Dec-01-25	-37	1	0%	0%	100%	0			Jan-27-26	Feb-09-26	14
SU-CP-111	REVIEW & APPROVE - WASTE CONTAINERS (CDI	14	Jan-20-26 A	Jan-23-26 A	Nov-18-25	Dec-01-25		1	100%	100%	100%	3	Jan-20-26	Jan-23-26	Jan-27-26	Jan-27-26	3
SU-CP-112	REVIEW & APPROVE - BLEACHERS (CDP)	14	Dec-31-25 A	Jan-15-26 A	Nov-18-25	Dec-01-25		1	100%	100%	100%	15	Dec-31-25	Jan-15-26	Jan-27-26	Jan-27-26	15
UpDT_01/27/26_Rev.5.11.12	FABRICATION & DELIVERY - COLON	225	Sep-22-25 A	May-18-26	Oct-09-25	Jan-26-26	-76	18			0%	127	Sep-22-25		Jan-27-26	May-18-26	239
UpDT_01/27/26_Rev.5.3	SUBMITTALS - COUNTRY L	123	Jan-20-26 A	Apr-24-26	Nov-05-25	Mar-16-26	19	48			0%	3	Jan-20-26		Jan-27-26	Apr-24-26	95
UpDT_01/27/26_Rev.5.9	CONSTRUCTION	326	Oct-06-25 A	Aug-27-26	Oct-06-25	May-22-26	-97	65			63.94%	98	Oct-06-25		Jan-27-26	Aug-27-26	326
UpDT_01/27/26_Rev.5.9.10	COLONIAL DRIVE PARK - Overall Dur	182	Oct-06-25 A	Jun-22-26	Oct-06-25	Feb-27-26	-67	40			89.31%	67	Oct-06-25		Jan-27-26	Jun-22-26	182
UpDT_01/27/26_Rev.5.9.10.1	MOBILIZATION - COLONIAL DRIVE P	7	Oct-06-25 A	Oct-28-25 A	Oct-06-25	Oct-28-25		3			100%	16	Oct-06-25	Oct-28-25	Jan-27-26	Jan-27-26	16
CP-100	MOBILIZATION AND SITE PROTECTION - COLONI	6	Oct-06-25 A	Oct-13-25 A	Oct-06-25	Oct-13-25		1	100%	100%	100%	5	Oct-06-25	Oct-13-25	Jan-27-26	Jan-27-26	5
CP-102	GPR - COLONIAL DRIVE PARK	7	Oct-14-25 A	Oct-22-25 A	Oct-14-25	Oct-22-25		1	100%	100%	100%	6	Oct-14-25	Oct-22-25	Jan-27-26	Jan-27-26	6
CP-103	INSTALL BARRICADE PROTECTION - COLONIAL I	4	Oct-23-25 A	Oct-28-25 A	Oct-23-25	Oct-28-25		1	100%	100%	100%	3	Oct-23-25	Oct-28-25	Jan-27-26	Jan-27-26	3
UpDT_01/27/26_Rev.5.9.10.2	SITE IMPROVEMENT - COLONIAL D	128	Oct-06-25 A	Apr-06-26	Oct-14-25	Jan-26-26	-27	22			100%	67	Oct-06-25		Jan-27-26	Apr-06-26	128
UpDT_01/27/26_Rev.5.9.10.2.3	CONCRETE WORK - COLONIAL	95	Oct-06-25 A	Feb-18-26	Oct-14-25	Dec-09-25	-17	9			100%	67	Oct-06-25		Jan-27-26	Feb-18-26	95
UpDT_01/27/26_Rev.5.9.10.2.3.1	SLABS ADA PICNIC TABLE	6	Oct-06-25 A	Oct-14-25 A	Oct-14-25	Oct-21-25		1			100%	6	Oct-06-25	Oct-14-25	Jan-27-26	Jan-27-26	6
CP-118	FORM, REINFORCE, POUR CONCRETE SLAB - AI	6	Oct-06-25 A	Oct-14-25 A	Oct-14-25	Oct-21-25		1	100%	100%	100%	6	Oct-06-25	Oct-14-25	Jan-27-26	Jan-27-26	6
UpDT_01/27/26_Rev.5.9.10.2.3.2	SLABS BLEACHERS - COL	15	Oct-06-25 A	Nov-21-25 A	Oct-14-25	Nov-03-25		1			100%	34	Oct-06-25	Nov-21-25	Jan-27-26	Jan-27-26	34
CP-120	FORM, REINFORCE, POUR CONCRETE SLAB - AI	15	Oct-06-25 A	Nov-21-25 A	Oct-14-25	Nov-03-25		1	100%	100%	100%	34	Oct-06-25	Nov-21-25	Jan-27-26	Jan-27-26	34
UpDT_01/27/26_Rev.5.9.10.2.3.3	SLAB BENCHES - COLONI	4	Dec-05-25 A	Jan-12-26 A	Nov-04-25	Nov-07-25		1			100%	24	Dec-05-25	Jan-12-26	Jan-27-26	Jan-27-26	24
CP-122	FORM, REINFORCE, POUR CONCRETE SLAB - AI	4	Dec-05-25 A	Jan-12-26 A	Nov-04-25	Nov-07-25		1	100%	100%	100%	24	Dec-05-25	Jan-12-26	Jan-27-26	Jan-27-26	24
UpDT_01/27/26_Rev.5.9.10.2.3.4	CONCRETE WALKWAYS - (	95	Nov-18-25 A	Feb-18-26	Nov-10-25	Dec-09-25	-17	6			100%	11	Nov-18-25		Jan-27-26	Feb-18-26	64
CP-124	DEMOLITION EXISTING ASPHALT WALKWAYS - C	3	Nov-18-25 A	Nov-18-25 A	Nov-10-25	Nov-12-25		1	100%	100%	100%	0	Nov-18-25	Nov-18-25	Jan-27-26	Jan-27-26	0
CP-12	ASPHALT WALKWAY REPAIR - COLONIAL DRIVE I	3	Feb-10-26	Feb-12-26	Nov-13-25	Nov-17-25	-17	1	0%	0%	100%	0			Feb-10-26	Feb-12-26	3
CP-123	DEMOLITION EXISTING CONCRETE WALKWAYS -	1	Feb-13-26	Feb-13-26	Nov-18-25	Nov-18-25	-17	1	0%	0%	100%	0			Feb-13-26	Feb-13-26	1
CP-125	FORM, REINFORCE, POUR CONCRETE SLAB - W	2	Nov-19-25 A	Nov-20-25 A	Nov-19-25	Nov-20-25		1	100%	100%	100%	1	Nov-19-25	Nov-20-25	Feb-13-26	Feb-13-26	1
CP-12	POURING FIBER CONCRETE SLAB - WALKWAY -	9	Nov-21-25 A	Dec-04-25 A	Nov-21-25	Dec-04-25		1	100%	100%	100%	8	Nov-21-25	Dec-04-25	Feb-13-26	Feb-13-26	8
CP-126	INSTALL HAND RAILING RAMPS - COLONIAL DRI	3	Feb-16-26	Feb-18-26	Dec-05-25	Dec-09-25	-17	1	0%	0%	100%	0			Feb-16-26	Feb-18-26	3
UpDT_01/27/26_Rev.5.9.10.2.1	NEW WATER LINES - COLONIAL	11	Nov-26-25 A	Dec-19-25 A	Nov-11-25	Dec-08-25		3			100%	16	Nov-26-25	Dec-19-25	Jan-27-26	Jan-27-26	16
UpDT_01/27/26_Rev.5.9.10.2.4	DRYWELL SYSTEM - COLONIAL	22	Jan-27-26	Feb-25-26	Dec-09-25	Dec-24-25	-22	5			100%	0			Jan-27-26	Feb-25-26	22
UpDT_01/27/26_Rev.5.9.10.2.5	ADA SITE FURNISHING - COLON	28	Feb-26-26	Apr-06-26	Dec-26-25	Jan-26-26	-27	5			100%	0			Feb-26-26	Apr-06-26	28
UpDT_01/27/26_Rev.5.9.10.4	RECREATION CENTER RENOVATIO	69	Feb-25-26	Jun-02-26	Dec-17-25	Feb-09-26	-67	7			83.31%	0			Feb-25-26	Jun-02-26	69
UpDT_01/27/26_Rev.5.9.10.6	DUGOUTS MODIFICATION & CHAIN	12	Apr-08-26	Apr-23-26	Jan-15-26	Jan-30-26	-38	3			53.3%	0			Apr-08-26	Apr-23-26	12
UpDT_01/27/26_Rev.5.9.10.5	FENCES & GATES - COLONIAL DRI	7	Jun-03-26	Jun-11-26	Feb-10-26	Feb-18-26	-67	2			0%	0			Jun-03-26	Jun-11-26	7
UpDT_01/27/26_Rev.5.9.10.3	CDP COMPLETION & CLOSEOUT - (	7	Jun-12-26	Jun-22-26	Feb-19-26	Feb-27-26	-67	3			0%	0			Jun-12-26	Jun-22-26	7
UpDT_01/27/26_Rev.5.9.1	COUNTRY LAKE PARK - Overall Durati	183	Feb-26-26	Aug-27-26	Jan-13-26	May-22-26	-97	25			39.97%	0			Feb-26-26	Aug-27-26	183
UpDT_01/27/26_Rev.5.10	PROJECT COMPLETION &	72	Aug-27-26	Nov-07-26	May-23-26	Aug-02-26	0	6			0%	0			Aug-27-26	Nov-07-26	72
PC-100	PROJECT FINAL INSPECTION	12	Aug-27-26	Sep-08-26	May-23-26	Jun-03-26	-97	1	0%	0%	0%	0			Aug-27-26	Sep-08-26	12
PC-101	PROJECT FINAL SUBSTANTIAL COMPLETION - TC	0		Sep-08-26*		Jun-03-26	-97	1	0%	0%	0%	0				Sep-08-26	0
PC-101-1	A/E & MDC-PROS PUNCH LIST WALKTHROUGH	10	Sep-08-26	Sep-18-26	Jun-04-26	Jun-13-26	0	1	0%	0%	0%	0			Sep-08-26	Sep-18-26	10
PC-113	PROJECT FINAL PUNCH LIST, CORRECTION AND	45	Sep-18-26	Nov-02-26	Jun-14-26	Jul-28-26	0	1	0%	0%	0%	0			Sep-18-26	Nov-02-26	45
PC-113-1	MDC-PROS FINAL CERTIFICATION OF OCCUPAN	5	Nov-02-26	Nov-07-26	Jul-29-26	Aug-02-26	0	1	0%	0%	0%	0			Nov-02-26	Nov-07-26	5
PC-102	PROJECT FINAL COMPLETION (AUG-2-26)	0		Nov-07-26		Aug-02-26	0	1	0%	0%	0%	0				Nov-07-26	0
